

Morton County Road Commission Agenda

Morton County Highway Department, 2916 37th St NW, Mandan ND

20 December 2023 @ 9:00 am

Call to order

Roll Call

Approval of Agenda

Approval of minutes for the previous meeting

1. Public Hearing on Sturn Section Line Vacation;
2. Review Revised Master Plan & Currently Proposed Phase 23 Subdivision;
3. Discuss Partial Vacation of Section Line – James Bendish;
4. Discuss Stark Bridge Bids;
5. Monthly Updates:
 - a. Design Projects
 - b. Construction Projects
 - c. Culvert Replacements
 - d. Budget Update

Morton County Road Commission Meeting
Morton County Highway Department, 2916 37th St NW, Mandan, ND 58554
November 15, 2023

Commission members Present: Jackie Buckley (telephone), Kyle Kirchmeier, Steve Tomac

Commission members Absent: Ron Leingang, Roger Hille

Others present: John Saiki, Chad Schneider

The meeting was called to order at 9:00 am by Vice-Chair Jackie Buckley

Steve made a motion to approve the agenda. Kyle 2nd. Motion carried.

Kyle made a motion to approve the minutes. Steve 2nd, motion carried.


1. Discuss 2nd Approach Permit, for Kevin Miller, in High Chaparral Estates – Due to Ron and Roger being absent, the remaining commissioners decided to revisit this item at the next meeting, when all commissioners should be in attendance.
2. Discuss Morton County Highway Department Policies present to the County Commission at the November 9th meeting – Decided that the original versions of the policies will be marked up with changes and presented at a future commission meeting.
4. Monthly Updates – a & b. Design Projects and Construction projects – Bridges near Flasher and St Anthony are under contract with APEX. Structure type has been selected. Sauber has completed PS & E plans for the Stark bridge, schedule for February Bid Opening. Solen was bid for the third time, no bids. Bridge South of Almont (Sauber Engineering) selected Alignment. Youngtown (AE2S Engineering), plans have been submitted to the NDDOT. Little Heart Bridge – Box culvert has been installed and Martin Construction is finishing up the backfilling. Bridge north of the Truck Stop (Sauber) – The States Attorneys office sent a letter to the Bonding Company seeking at least the 5 percent Bid Bond. No response from the Bonding Company. At this point Morton County will cash the Bid Bond, follow up with the Bonding Company regarding a Performance Bond that was not forwarded to the County. The bridge on County Road 80, awarded to Midwest Construction, work is complete and the road is open. The bridges SW of Fort Rice, awarded to Edward Schwartz, both box culverts are completed and the road is opened. Bridge North of Mandan (Mork) with (KLJ), Road Commission agreed to straighten out road. Road Commission agreed that KLJ is entitled to an additional \$35,000, will have to follow up with KLJ. Bridge W of Vern Leingang (Moore Engineering), work is in progress. Should complete installation today start backfilling. The bridge near Danzig Dam (SRF), received information from SRF that the COE will not approve a permit for a project that fills the channel, such as an RCB. The replacement bridge will have to be a bridge that is at least as long as the existing bridge. Design of this project has been paused indefinitely. Bridge North of Glen Ullin on the frontage road, NDDOT working on easement options since a portion of one of the wing

walls will be on NDDOT (I-94) right of way. Bismarck District sent the permit to FHWA for review and concurrence.

- c. Culvert Replacements – Work is wrapped up for the year.
- d. Budget Update – Overtime, Salary and Stock Items are the budget lines that have been exceeded. There will be some large charges in the next 6 weeks with the Box Culvert work being completed.

Kyle moved to adjourn, Steve 2nd. The meeting was adjourned 9:25 am.


Sturn Section Line Vacation Request (subdivision in pink)

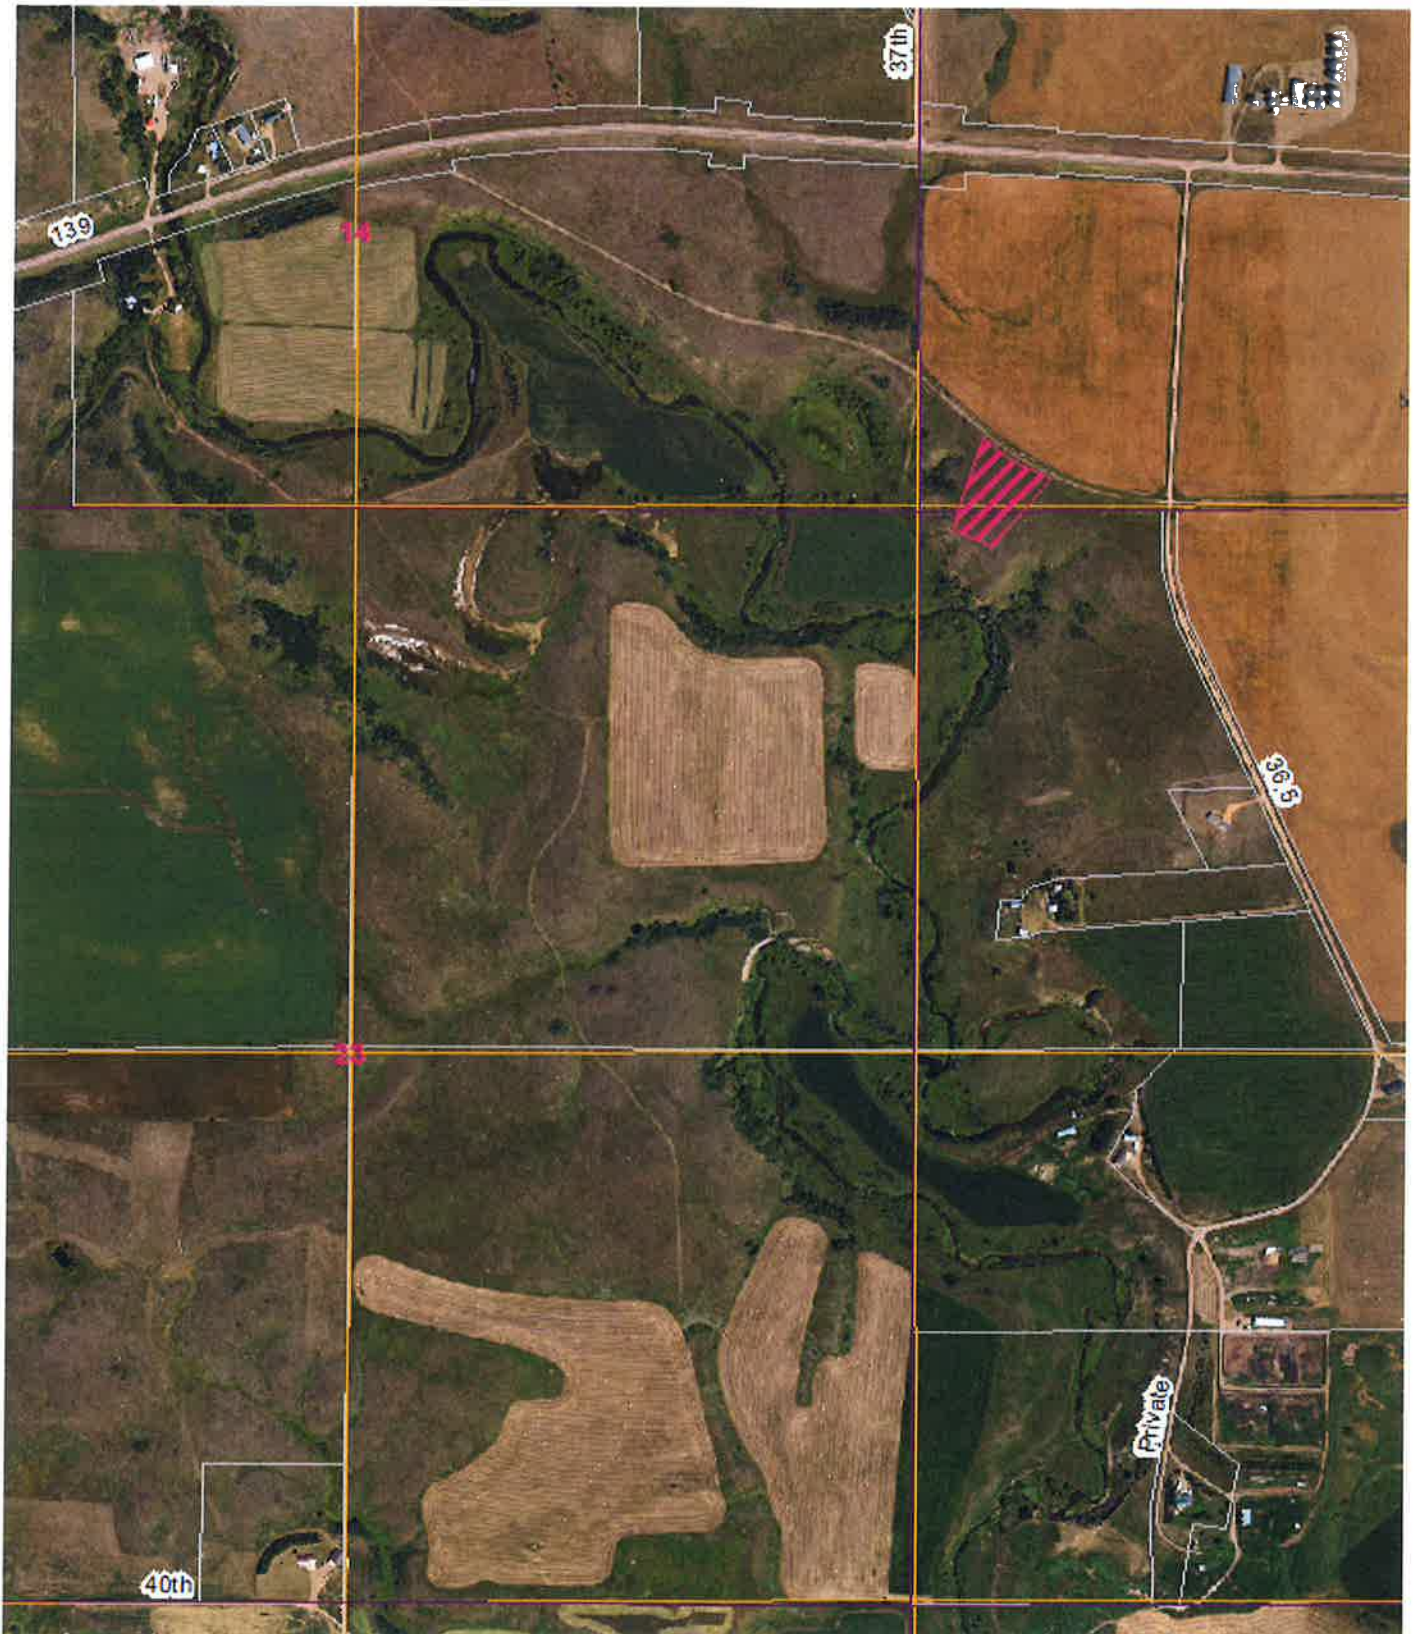


PRELIMINARY PLAT OF HARMON VILLAGE 23RD SUBDIVISION

OF MORTON COUNTY, NORTH DAKOTA
PART OF THE W1/2 OF SECTION 12, T140N-R82W, MORTON COUNTY, NORTH DAKOTA

NM14
SEC. 12

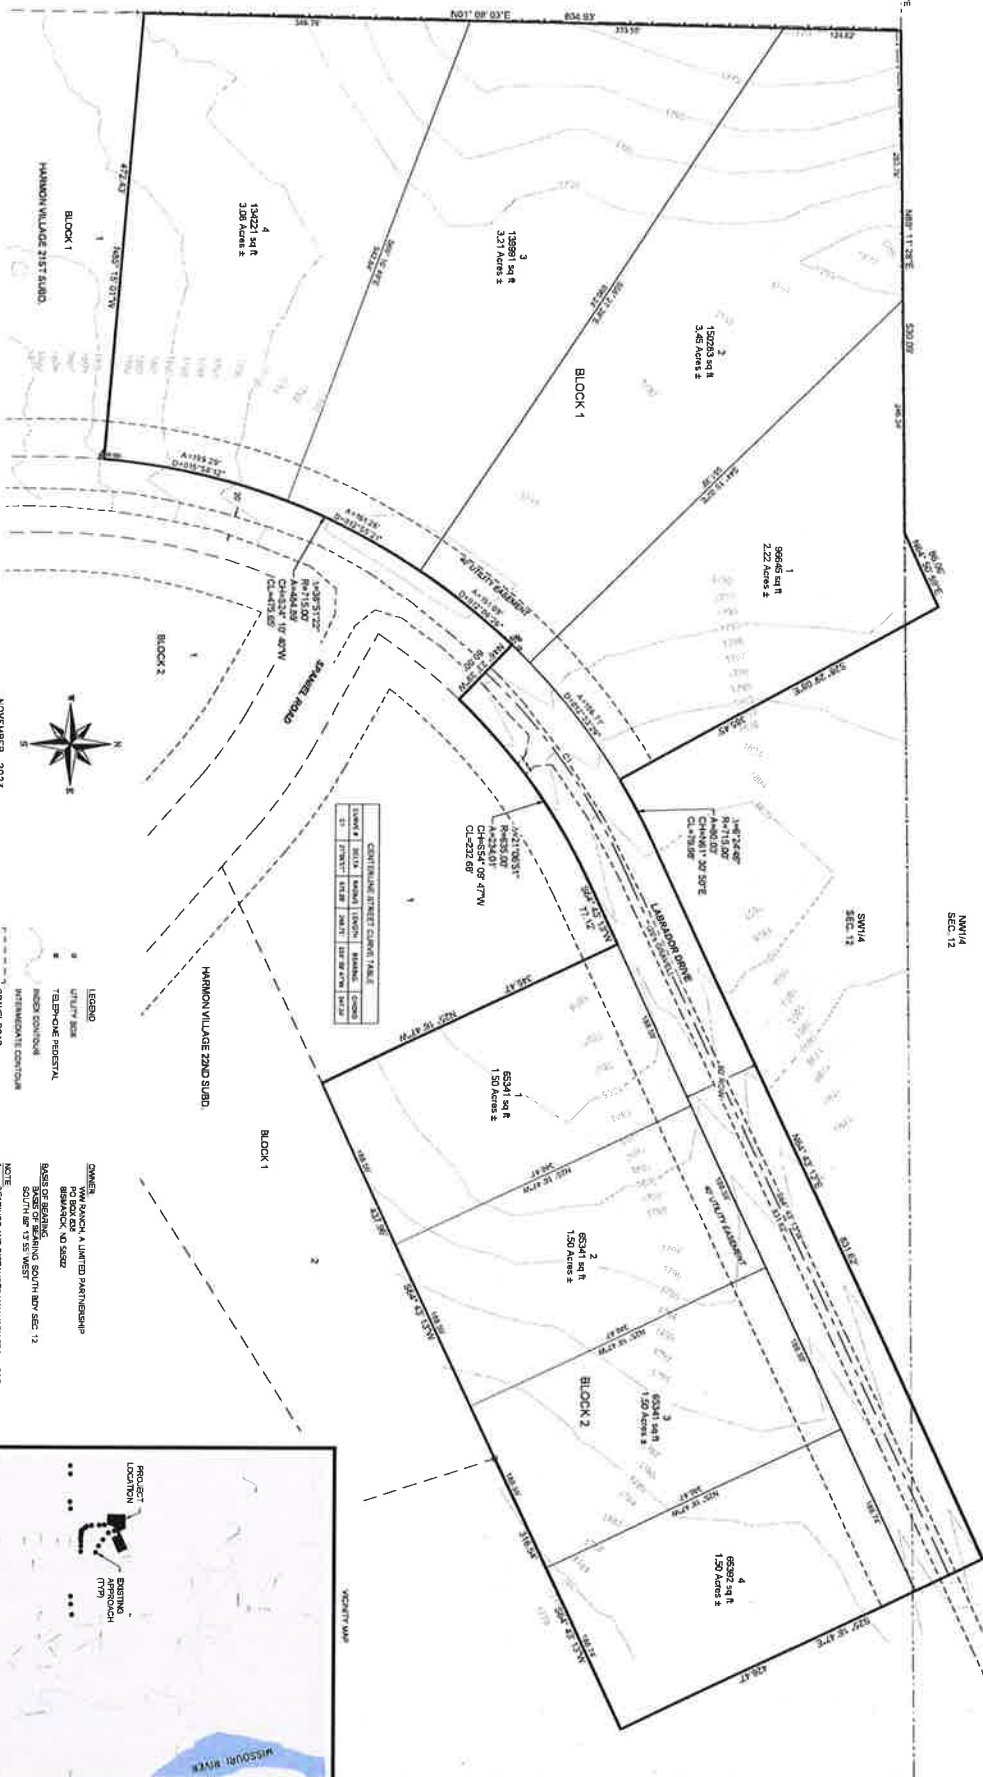

STAKE #	DATE	MARK	LOCATION	BEARING	LENGTH
1	11/15/07	WOOD	CL-1785.00'	S 89° 52' 00" W	1785.00'
2	11/15/07	WOOD	CL-222.00'	S 89° 52' 00" W	222.00'




- LEGEND**
- UTILITY POLE
 - 7.5' BENCH MARK
 - 1" BENCH MARK
 - INTERSECTION CONTROL
 - DANIEL ROAD
 - TRAIL LINE

OWNER:
TWO RANCH, A LIMITED PARTNERSHIP
PO BOX 602
MORTON, ND 58502

SECTION:
SECTION 12 OF RANGE SOUTH AND SEC. 12
SOUTH 89° 52' 00" WEST

NOTE: BEARINGS AND DISTANCES WERE OBTAINED FROM PERMITS DOCUMENTS OF RECORD AND TO DIFFERENT METHODS
TOTAL STAKE 1" BENCH MARK
TOTAL ACRES 12.50

TOMAN ENGINEERING
501 1st Street NW, Mandan, ND 58554
Phone: 701-663-5463 Fax: 701-663-0923

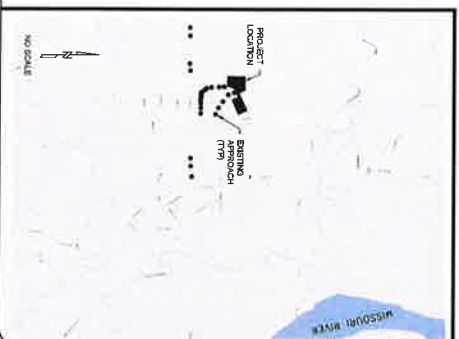

Morton County Covid Funding Bridge Priorities

Bridge #	Location	Notes	Consultant	Contact	Replacement a Major Structure	NDOT Project Number	PCN	Bid Year			
On System (80% Funded)	30-153-03.0 30-156-27.0	11 East 1 North Fuller 2 South 1 East of St. Anthony	ABEX	Troy Ripplinger	Selected Structure Type	X	8U-0090(050)	23716	2025		
	30-143-19.0 30-128-19.0	9 South 3 East of Judson 1 South Almont	Sauber	John Sauber	12/8/2023 Bid Opening Selected Alignment	X	BR-C-020(080) BR-C-027(056)	23734 23735	2024 2025	Received one Bid Docketed in 26 Budget under consultants	
2022	30-133-03.0	7N of New Salem	AEC5	Todd Morton	working Bridge Adoption	X	BR-C-020(049)	23557	2024		
2022	30-160-23.0	6N 4 E St. Anthony	Interstate	Maria Tomic	Minor finishing work	X	\$906,575.99				
2022	HB 1505 Funding	7N 13E of Judson	North of Truck Stop	Sauber	John Sauber	Bid for Construction in 2024	X	\$675,000 (estimate)	2023	Flex Funding Program	
		65 6W Ft Rice	2 sites combined	Sauber	John Sauber	Complete	X	\$1187,697.59			
		33 7W Ft Rice	CO RD 80	Sauber	John Sauber	Complete	X	\$553,414.00			
2022	HB 1505 Township Roads	2W 6N of Mandan	Bank Slumping	Jennie Krause	Contact regarding additional work for \$35,000		Construct 2025 or later		2024	set aside HB funds of	
2023	ABPA (COVID) Funding	2W 2N of St Anthony	W of Verm Leffingr	Moore	Miles Michoff	Complete	X	\$1,187,383.00			NO FUNDS CURRENTLY ALLOCATED FOR THIS
		30-123-05.0	9W 4N of New Salem	SFC	Ryan Rykowsky	NDOT sent Permit to FHWA for review have not heard	X			2024	NO FUNDS CURRENTLY ALLOCATED FOR THIS
		30-114-08.0	3N of Glen Ullin	Frontage Road	Apex	Troy Ripplinger					NO FUNDS CURRENTLY ALLOCATED FOR THIS
		30-128-10.0	3W 1S of New Salem	40th Street							NO FUNDS CURRENTLY ALLOCATED FOR THIS
		30-120-23.0	5S 8W of Almont	CO 87							NO FUNDS CURRENTLY ALLOCATED FOR THIS
		30-164-35.0	3S 9W of Fort Rice	17th Ave							NO FUNDS CURRENTLY ALLOCATED FOR THIS
2024	ABPA (COVID) Funding	City of Hebron	South Park Street	Closed						NO FUNDS CURRENTLY ALLOCATED FOR THIS	
		City of Hebron	East Fulton Ave	Closed						NO FUNDS CURRENTLY ALLOCATED FOR THIS	
		3N of Glen Ullin	Big Bridge West of Almont	Closed						NO FUNDS CURRENTLY ALLOCATED FOR THIS	

Bid and Construct in 2024
Under contract for Construction in 2023

Revised December 18, 2023
